


Portfolio Governance Is a Funding-Discipline Problem, Not a Reporting Problem

Why the portfolios that create value are the ones that can start, redirect, and stop investments on evidence — not the ones with the best dashboards

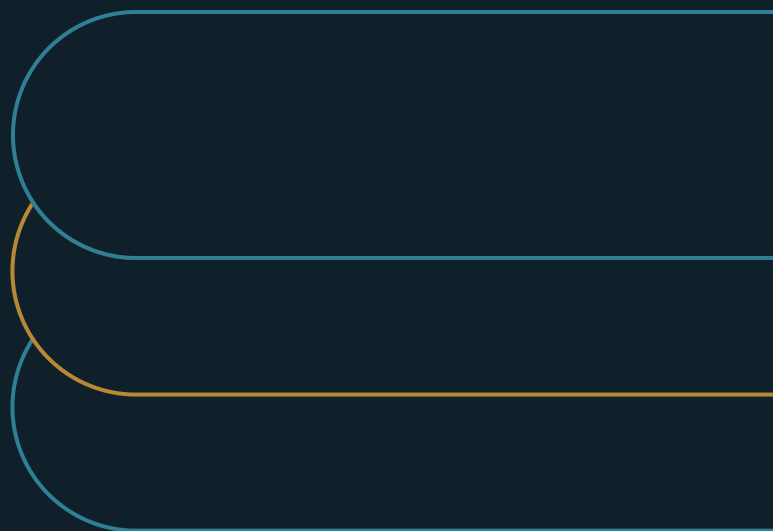

Marco Policani

Enterprise Portfolio · PMO · AI Operating Governance

policani.net · linkedin.com/in/marcpolicani

July 2026

EXECUTIVE SUMMARY

Funding discipline means choosing what to start, redirect, and stop on the evidence.

Most organizations produce status, not decisions. Funding discipline is the authority, the evidence, and the willingness to start, redirect, and stop investments. It is what separates a governed portfolio from a monitored one.

- 01** The kill decision is the test. A portfolio that stops nothing is accumulating, not setting priorities. Accumulation without subtraction spreads capacity too thin to matter.
- 02** Restore gates as funding decisions. Set the criteria in advance, match the evidence to the stage, and name a decision owner who can and will return a stop.
- 03** Set kill criteria when the project is funded, not when it is failing. Willingness has to be engineered before anyone is emotionally invested.

CONTENTS

Governance is a funding decision	AI spending needs the same discipline
Why reporting feels like governing	What this argument does not claim
What funding discipline means	How to make stopping possible
The kill decision is the test	The one-page funding decision
A gate has to be able to say no	The PMO's real job
Capacity is the real limit	Signals of a governed portfolio
What a portfolio review is for	From reporting to deciding
Two patterns from practice	Notes and sources

Governance is a funding decision

Most organizations believe they have a portfolio governance problem. What they have is a reporting habit. They can produce status. They have dashboards, RAG indicators, steering decks, and a monthly meeting where projects get reviewed. What they cannot reliably do is decide. Governance exists to settle what gets funded, what gets redirected, and what gets stopped¹, on the evidence, and to make the decision stick. Reporting describes the portfolio. Funding discipline

governs it. Confusing the two is the most common failure in portfolio management.

This paper argues that portfolio governance is fundamentally a funding-discipline problem. Knowing the status of the work is the easy part. The hard part is having the authority, the evidence, and the willingness to move money toward what is working and away from what is not. That includes killing projects that no longer earn their place. A portfolio that cannot stop things becomes a queue of commitments that only grows. Reporting on that queue more precisely does not make it governed.

This is deliberately a governance argument, not a tooling one. Better dashboards, more mature PPM software, and tighter status reporting can all sit alongside a portfolio that never kills anything and starves its best work of capacity. The established portfolio literature points the same way. Robert Cooper and Scott Edgett define new-product portfolio management as a dynamic process. Projects are evaluated, prioritized, accelerated, killed, or de-prioritized, and resources are allocated and re-allocated. They name doing the right projects as one of the two ways a business succeeds.²

Why reporting feels like governing

Reporting is seductive because you can see it, build it, and finish it. A good status view makes leaders feel governed. The work is accounted for, the risks are colored, the milestones are tracked. All of that can be true while no decision that matters is being made. A project can be red for months and keep its funding. A low-value project can stay green and keep its capacity. The dashboard reports reality faithfully and changes nothing about it.

The trap deepens when reporting becomes the point of the governance meeting. A steering group that spends its hour rebuilding status has no time left to decide. It quietly redefines governance as showing up and being informed, rather than deciding where money goes. Everyone leaves informed and nothing leaves different. Over time the organization mistakes the ritual for the job. It believes it is governing the portfolio because it is meeting about the portfolio.

There is a structural reason this lasts. Reporting avoids the two hardest acts in portfolio management: saying no to a new thing, and stopping an existing one. Both create friction. Both disappoint a sponsor. Both make someone defend a judgment. A dashboard asks for none of that. An organization can build an elaborate reporting machine precisely, if unconsciously, to avoid the decisions that reporting is meant to inform. The tell is simple. If the portfolio review rarely changes where the money and the people go, it is a reporting exercise wearing a governance label.

What funding discipline means

Funding discipline can be defined precisely, which is what makes it governable:

EXHIBIT 1

Funding becomes governance when evidence can move it**01****Name value and problem**

Say what outcome will change before money or capacity moves.

02**Rank the whole portfolio**

Compare value, risk, and the capacity you actually have.

03**Fund the next round**

Release only what the next piece of evidence can justify.

04**Own the benefit**

Name the person accountable for the value claim.

05**Continue, redirect, stop**

Return money and capacity to the portfolio when evidence changes.

Funding discipline is the authority, the evidence, and the willingness to start, continue, redirect, and stop investments on their expected and demonstrated value. Each decision has a named owner, and the organization has the resolve to make the decision real. If any of the three — authority, evidence, or willingness — is missing, the portfolio is monitored rather than governed.

Each part fails in its own way. Without authority, the forum can recommend but cannot move money, and decisions vanish on contact with a powerful sponsor. Without evidence, decisions turn political, settled by confidence and volume rather than value. Cooper and Edgett list better objectivity in project selection, “to weed out bad projects,” among the reasons portfolio management matters.² Without willingness, an organization has the authority and the evidence and still cannot bring itself to stop a project that is visible, sponsored, and loaded with sunk cost. All three have to be present, and the third, willingness, is the one no tool can supply.

Funding discipline is also continuous, not annual. Set the portfolio budget once a year and money is committed long before the evidence that should govern it exists. It then stays committed long after the evidence has turned. McKinsey’s guidance on realizing AI value makes the same point in a modern setting: build value in up front, backed by evidence packs and staged decisions, rather than assuming it at funding and hoping for it at the end.³ The principle carries well beyond AI. Money should follow the evidence rather than last year’s split.⁴ The model is closer to how a venture fund works than to how an annual budget works: money released in stages against evidence, with standing authority to stop a losing bet early and put more behind a winning one. Here it runs inside one enterprise portfolio rather than across a fund of startups.

The kill decision is the test

The sharpest test of whether a portfolio is governed is whether it can kill things. Starting projects is easy and popular; every sponsor wants a yes. Stopping them is where discipline either exists or does not. A portfolio that funds a hundred things and stops none of them has quit setting priorities and started accumulating. Accumulation without subtraction is how capacity gets spread so thin that nothing important moves fast enough to matter.

Cooper and Edgett build the kill decision into the system rather than treating it as an exception: Go/Kill decisions on individual projects are made on an ongoing basis, and resources are allocated and re-allocated among active projects.² The reason this is hard is entirely human. Killing a project means disappointing its sponsor, accepting sunk cost, and admitting an earlier decision did not pan out. Those are real costs. A governance system that does not explicitly make room for them will default to letting weak work live, because letting it live is the easier path.

One signal is worth watching: the portfolio's stop rate. A system that never kills anything rarely reflects unusually good judgment at intake. More often it has quietly decided not to govern.

A gate has to be able to say no

Stage gates are widely adopted and widely defanged. Used as designed, a gate is a funding decision. The team brings evidence, and the gate decides whether to keep funding the work, redirect it, or stop it. In its degraded form, a gate is a checkpoint the project passes by showing up, because no one at the gate is actually willing to say no. A gate that cannot return a stop is only a milestone with a meeting attached.

EXHIBIT 2

A gate is a funding decision, not a milestone with a meeting

Designed form

The team brings evidence. The gate decides to keep funding, redirect, or stop. It can return a no.

Degraded form

A checkpoint the project passes by showing up, because no one at the gate is willing to say no.

Restoring the gate means restoring its power to withhold money. That takes three things reporting culture tends to erode. First, real decision criteria set in advance, so the gate does not turn on who argues best in the room. Second, evidence matched to the stage: early gates test signal, later gates test value actually realized, and neither pretends to prove everything at once. Third, a named decision

owner who can and will return a stop. McKinsey's staged, evidence-backed model of value realization is essentially this discipline applied rigorously: prove value in stages, and let the evidence at each stage govern the next increment of funding.³

Gates also protect against the most expensive pattern in delivery. It is the project that is clearly failing but too far along for anyone to stop informally. A working gate gives the organization a scheduled, legitimate, expected moment to stop that work before it eats another cycle of capacity. Without that moment, the failing project rides its own momentum to the end. Everyone involved can see it happening and no one has the standing to halt it.

Capacity is the real limit

Underneath funding sits the resource that is actually scarce: capacity, the limited supply of skilled people and attention that can do the work. The most common portfolio failure is taking on too much. The organization commits to more work than it can execute. Everything slows, the best people are spread across too many projects, and throughput collapses even though every single project looks funded. Funding discipline is, in practice, capacity discipline. Money is only real when there is capacity to turn it into outcomes.

That turns prioritizing into sequencing rather than selection. Which projects are worth doing is only half the question. The other half is which ones the organization can staff now, which should wait, and which should stop so the important work gets the capacity it needs. A portfolio that funds everything it approves, without checking whether the capacity exists to deliver it, has made a budgeting decision and called it a strategy. The discipline is to hold active commitments to what capacity can carry. Treat every new yes as implying a no or a not-yet somewhere else.

Capacity discipline is also where the kill decision pays off most visibly. Every project that should have been stopped and was not is capacity withheld from work that could move. Freeing that capacity is frequently a larger lever than new funding. It moves the scarcest resource to its highest-value use without spending another dollar. Leaders who feel starved of capacity are often, on inspection, over-committed rather than under-resourced.

What a portfolio review is for

The difference between a reporting culture and a funding-discipline culture shows up in what the portfolio review actually does. The table below pairs each artifact leaders tend to rely on with the funding question it quietly avoids.

The reporting artifact	What it tells you	The funding-discipline question it avoids
A RAG status dashboard	Which projects are troubled right now	Which troubled project should we stop, not just watch
A milestone tracker	Whether work is on schedule	Whether this work still deserves the capacity it holds
A budget-vs-actual view	How much has been spent	Whether the remaining spend beats the next-best use of it
A completed-projects count	How much the portfolio delivered	How much of it changed an outcome anyone funded
A packed roadmap	How much is planned	Whether we have the capacity to deliver any of it well

The right column is the governance work. Better reporting answers none of it. Deciding where the money and the capacity go answers all of it. A review that spends its time in the middle column is informed. One that spends its time in the right column is governed.

Two patterns from practice

The illustrations below are operating patterns, not named programs.

In the first, a portfolio review was redesigned so that most of the meeting went to decisions rather than updates. Status was written up first and read before the meeting. The meeting itself existed to decide what to continue, redirect, and stop. The effect was more decisions, and specifically more stops, which freed capacity that had been quietly trapped in work no one was willing to end. The dashboards did not improve. The willingness to act on them did.

In the second, funding moved from an annual commitment to a staged one. Projects earned the next increment by showing evidence, not by having been approved once at the start of the year. Weak projects surfaced earlier, because the next gate was never far away, and capacity moved toward work that was demonstrably paying off. The mechanism was ordinary stage-gate discipline used as designed: a funding decision rather than a status review.

AI spending needs the same discipline

This argument has become newly urgent. AI has produced a fresh wave of projects competing for the same scarce capacity, often funded on enthusiasm rather than evidence. Everything true of portfolio governance is true of AI portfolio governance, only more so. AI is new enough that it is especially easy to keep funding activity that is not yet producing value. McKinsey's own analysis argues that AI-driven productivity gains are becoming table stakes and that durable value comes from deeper reshaping — which is precisely a portfolio-selection judgment about where AI investment is worth making and where it is not.⁵

Treated as a funding-discipline problem, AI work faces the same tests as any other investment. Does it have a named owner? Is its value demonstrated in stages rather than assumed? Is the organization willing to stop the AI projects that are not earning their capacity? An AI portfolio that cannot kill a fashionable but unproductive pilot has the same problem as a traditional portfolio that cannot stop a sponsored but failing project. The cure is the same: move money on evidence, and be willing to stop.

What this argument does not claim

Two honest limits apply. First, the portfolio literature this paper draws on establishes the principles of go/kill discipline and capacity-constrained prioritization. It does not establish how much value weak funding discipline costs. That figure varies widely by organization and is not a single, transferable number. Treat published waste statistics with caution. Measure your own stop rate and capacity utilization rather than importing someone else's number. Second, funding discipline is necessary without being sufficient on its own. A portfolio can move money crisply on evidence and still choose the wrong strategy. Discipline governs how investment decisions are made, not whether the underlying bets are wise. This paper argues for the mechanism, not for any particular portfolio's choices.

How to make stopping possible

Authority and evidence can be designed. Willingness has to be engineered, because it is the part human nature resists. The most reliable way to make stopping possible is to set the conditions for stopping early. Decide them when the project is funded, before anyone is emotionally invested, not at the painful moment it is failing. With explicit, pre-committed kill criteria at the gate, stopping later enforces an agreement the sponsor already accepted. It is not a verdict against them personally. That one change removes much of the friction that keeps weak work alive, because the decision was made when it was cheap and impersonal.

The second move is to change what a stop means. In most cultures a killed project reads as a failure, which is exactly why leaders avoid producing them. A governed portfolio treats a stop as capacity

recovered. The resources are not lost; they return to the pool and go to stronger work, which is the portfolio working as designed. Leaders who talk about stops this way, and who visibly celebrate a well-timed kill rather than quietly burying it, make the next stop easier and the whole system more honest.

The third move is to keep a capacity ledger beside the funding ledger, so every yes is visibly charged against a finite supply. Then the organization can see that approving a new project means pulling capacity off an existing one. The question shifts. It is no longer whether the new thing is good on its own — almost everything is — but whether it is better than what it would displace. That comparison is the essence of portfolio judgment, and it stays invisible until capacity is tracked as explicitly as money.

The one-page funding decision

Funding discipline becomes practical when every project arrives at every gate with the same short document. Then the decision turns on merits rather than on who prepared the most persuasive deck. A workable one-pager does five things. It states the outcome the project is meant to change, and the evidence that it is changing it. It gives the value expected and the value shown so far. It shows the capacity the project holds now and what that capacity would otherwise do. It records the pre-committed criteria that would justify stopping or redirecting it. And it names the owner accountable for the value claim. If the page cannot be filled in, the project is not ready for the funding it is asking for, and that gap is itself a finding.

The point of the page is symmetry, not bureaucracy. When every project answers the same questions, the portfolio can compare them honestly. The loudest sponsor loses the advantage that an unstructured review hands to whoever argues best. This is the discipline that intake and value-realization practice already recommend, applied at the funding gate. A decision is only as good as the evidence it is required to show. Requiring the same evidence of everything is what makes a portfolio a portfolio rather than a set of separately negotiated commitments.

The PMO's real job

Funding discipline changes what a portfolio management office is for. In a reporting culture, the PMO becomes a status factory. It collects updates, formats decks, chases red items, and measures its worth by how complete its reporting is. That work is real, but it is administrative, and it leaves the PMO outside the decisions that matter. In a funding-discipline culture, the PMO owns the integrity of the decision itself. It makes sure every project arrives at the gate with comparable evidence. It checks that the pre-committed kill criteria are actually applied, and that capacity is tracked honestly against commitments.

That is a shift from producing information to making sure decisions are made well. The PMO becomes the guardian of symmetry — the one group that will not let a well-connected sponsor skip the evidence

everyone else has to show. It keeps the capacity ledger that makes trade-offs visible. It also holds the memory of stops: which projects were killed, why, and what the freed capacity went on to do. That record is what turns stopping from a stigma into a track record. A PMO that owns this sits at the center of strategy. A reporting-only PMO does not.

Signals of a governed portfolio

Funding discipline is cultural as much as procedural, so it helps to name the signs leaders can actually observe in their own portfolio. A governed portfolio tends to show behaviors that a reporting-only portfolio cannot fake for long.

EXHIBIT 3

Six signals a reporting-only portfolio cannot fake for long

- 1 **Stops happen on schedule**
A stop counts as the system working, not as a failure to be buried.
- 2 **The meeting decides**
Most of the hour moves money and capacity. Status was read in advance.
- 3 **Same evidence for everyone**
Decisions track merit, not how persuasive a sponsor is.
- 4 **Capacity is tracked like budget**
Each new commitment is visibly charged against a finite supply.
- 5 **Kill criteria are set at funding**
Stopping enforces an agreement instead of delivering a verdict.
- 6 **Funding moves in stages**
Money is released in evidence-backed stages, not one annual commitment that outlives its evidence.

None of these signals is about the quality of reporting. A portfolio can score well on all of them with ordinary dashboards. That is the point. The behaviors, not the polish of the status, separate a portfolio that is governed from one that is merely watched. A leader who wants to know which kind they have should not look at the dashboard. They should look at how often, and how cleanly, the portfolio changes where its money and its people go.

From reporting to deciding

Better reporting is not what makes a portfolio create value. On that front many organizations are already over-invested, producing status no one turns into decisions. The portfolios that create value can move money and capacity toward what is working and away from what is not. They treat the kill decision as the system working rather than failing. And they hold their commitments to what their capacity can actually deliver.

Reporting tells you where the portfolio is. Funding discipline decides where it goes. The first is a camera. The second is a hand on the wheel, and no quality of camera substitutes for a hand on the wheel. Build the authority, the evidence, and the willingness to start, redirect, and stop investments on their merits, and the portfolio becomes a governed instrument of strategy. Skip it, and the organization will keep meeting about a portfolio it is not actually steering.

Notes and sources

1. Project Management Institute, The Standard for Portfolio Management, Third Edition, 2013. <https://www.pmi.org/-/media/pmi/documents/public/pdf/certifications/standard-for-portfolio-management-third-edition.pdf>
2. Robert G. Cooper and Scott J. Edgett, "Portfolio Management: Fundamental for New Product Success," Stage-Gate International. <https://www.stage-gate.com/blog/portfolio-management-fundamental-for-new-product-success/>
3. Johannes-Tobias Lorenz, Joshan Cherian Abraham, Robert Levin, and Douglas Ziman, "From promise to impact: How companies can measure—and realize—the full value of AI," McKinsey & Company, April 24, 2026. <https://www.mckinsey.com/capabilities/quantumblack/our-insights/from-promise-to-impact-how-companies-can-measure-and-realize-the-full-value-of-ai>
4. Stephen Hall, Dan Lovallo, and Reinier Musters, "How to Put Your Money Where Your Strategy Is," McKinsey & Company, March 1, 2012. <https://www.mckinsey.com/capabilities/strategy-and-corporate-finance/our-insights/how-to-put-your-money-where-your-strategy-is>
5. Antoine Montard, Dago Diedrich, and Tanguy Catlin, "Where AI will create value—and where it won't," McKinsey Quarterly, April 29, 2026. <https://www.mckinsey.com/capabilities/strategy-and-corporate-finance/our-insights/where-ai-will-create-value-and-where-it-wont>

About the author

Marco Policani is an enterprise portfolio, PMO, and AI operating-governance leader. He builds portfolio governance systems where AI carries the analytical load and named humans own every decision — an approach documented across case studies, walkthroughs, and working governance guides on his portfolio site.

Portfolio & governance library: policani.net/governance · Full portfolio: policani.net · LinkedIn: linkedin.com/in/marcpolicani

This white paper may be shared freely with attribution. © 2026 Marco Policani.
